



City of Rockwall
The New Horizon

ADDENDUM TO RFP

RFP Title: BID No. 1014-03-063 – FM 740 RIDGE RD MEDIAN
LANDSCAPE IMPROVEMENTS PROJECT

RFP Due: **2:00 pm CST, Thursday, July 30, 2026**

Addendum No.: 2

Issued (Date): July 29, 2026

TO BIDDER: This Addendum is an integral part of the RFP package under consideration by you as a Bidder in connection with the subject matter herein identified. The City of Rockwall deems all sealed proposals to have been proffered in recognition and consideration of the entire RFP package – **including all addenda**. For purposes of clarification, **receipt of this present Addendum by a Bidder should be evidenced by returning it (signed) as part of the Bidder's sealed proposal**. If the Proposal has already been received by The City of Rockwall Purchasing Department, Bidder should return this addendum in a separate sealed envelope, clearly marked with the RFP Title, and Opening Date and Time, as stated above.

**Reason for Issuance of this addendum: Clarifications to Bid Item 0192
Description Codes 7009 and 7003**

The information included herein is hereby incorporated into the documents of this present Bid matter and supersedes any conflicting documents or portion thereof previously issued.

Receipt of this Addendum is hereby acknowledged by the undersigned Bidder:

Authorized Signature (Bidder)

Title of Person Signing Above

Typed Name of Business or Individual

Date: _____

Address

CLARIFICATIONS AS FOLLOWS:

BID TAB ITEM No. 0192, Description Code 7009 | PLANT BED PREP:

TO BE PERFORMED PER TXDOT ITEM 192 LANDSCAPE PLANTING, SECTION 3.13 PLANT BED PREPARATION. PREPARE THE BED AND INSTALL THE PLANTING SOIL MIX, VEGETATION BARRIER, AND OTHER MATERIALS AS SHOWN ON THE PLANS.

BID TAB ITEM No. 0192, Description Code 7003 | PLANTING SOIL MIX | 16" DEPTH AMENDED SOIL (REFER TO SHEET 5) – ASSOCIATED WITH PLANTING BEDS:

EXISTING TOPSOIL (APPROX. 16") TO BE AMENDED WITH SOIL MIX, AS FOLLOWS:

- PRODUCT (APPROVED PLANTING SOIL MIX):
 - SANDY LOAM CLASSIFICATION AS: 45-50 % SAND, 20-25% SILT. 20-25% CLAY AND 4-6 ORGANIC MATTER. AMENDMENTS (IF REQUIRED) ADDED MUST BE LAB IDENTIFIED VIA. TESTING PRIOR TO FINAL MIX.
- SUPPLIER:
 - LIVING EARTH, SOIL BUILDING SYSTEMS OR APPROVED EQUAL; LIVING EARTH
 - CONTACT: PAUL TOMASO (972-869-4332), LIVING EARTH
 - CONTACT: BARON ABLON (972-831-8181), SOIL BUILDING SYSTEMS
- NOTE:
 - PROPOSED SOIL WILL REQUIRE TESTING EXISTING ON FOR NUTRIENT LEVELS AND pH CONDITIONS HAVE CHANGED.
 - FINAL MIX TO BE EXAMINED BY LANDSCAPE ARCHITECT FOR: NUTRIENT LEVELS, PH, BULK DENSITY, CLASSIFICATION. FOR PARTICLE SIZE BALANCE (SAND-SILT-CLAY %'S). INFILTRATION, AIR POROSITY, AND WATER HOLDING. AMENDMENTS ADDED MUST BE CHECKED WITH FINAL PLANTING.
 - FULL DEPTH OF NEW PLANTING BED BERMS TO BE CONSTRUCTED UTILIZING THE APPROVED PLANTING SOIL MIX.

FOLLOWING PAGES HAVE BEEN CLOUDED TO HIGHLIGHT MODIFIED QUANTITIES ASSOCIATED WITH BOTH ADDENDUM #1 AND #2:

- Addendum#2_CSJ1014-03-063_Bid Form
- Addendum#2_CSJ1014-03-063_Contract Time Estimate
- Addendum#2_CSJ1014-03-063_Sheets6&7

Item No.	Description Code	Name of Pay Item with Unit Price in Words	Bid Quantity	Unit	Unit Bid Price	Amount Bid
BASE BID						
0500	7001	MOBILIZATION	1	LS		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
		CONSTRUCTION CONTINGENCY	5%	of construction cost		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0100	7001	PREPARING ROW	50.00	STA		
		Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0100	7003	PREP ROW (TREE REMOVE) (0"-12" DIA)	138	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0192	7007	SOIL AMEND	1,199	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0556	7009	PIPE UNDERDRAINS (TY 9)(6")	3,245	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0194	7010	RDSIDE AMENITY (BOULDER)	39	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0194	7011	RDSIDE AMENITY (STONE SLAB)	5,541	SF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0192	7052	PLANT MATERIAL (MIN 3" CAL)(B&B)	121	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0192	7009	PLANT BED PREP	2,889	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0192	7016	LANDSCAPE EDGING	764	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				
0192	7022	LOOSE AGGR GRND COVER	1000	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and			\$	\$
		_____ Cents per unit				

Item No.	Description Code	Name of Pay Item with Unit Price in Words	Bid Quantity	Unit	Unit Bid Price	Amount Bid
0192	7026	PLANT MATERIAL (4" FLAT)	14,602	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$
0192	7026	PLANT MATERIAL (14/16 BULBS)	23,959	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$
0192	7026	PLANT MATERIAL (1 GAL)	16,594	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$
0192	7028	PLANT MATERIAL (3 GAL)	239	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$
0192	7002	MULCH	2,889	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$
0192	7003	PLANTING SOIL MIX	1,589	CY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$
0170	7001	IRRIGATION SYSTEM	1	LS		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$
0618	7045	CONDT (PVC) (SCH 40) (6") (BORE)	117	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and _____ Cents per unit			\$	\$

2

Item No.	Description Code	Name of Pay Item with Unit Price in Words	Bid Quantity	Unit	Unit Bid Price	Amount Bid
TRAFFIC CONTROL						
0502	7001	BARRICADES, SIGNS AND TRAFFIC HANDLING	12.2	MO		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0503	7001	PORTABLE CHANGEABLE MESSAGE SIGN	375	DAY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
EROSION CONTROL						
0506	7039	TEMP SEDMT CONT FENCE (INSTALL)	1,186	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0506	7040	TEMP SEDMT CONT FENCE (INLET PROTECTION)	527	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0506	7041	TEMP SEDMT CONT FENCE (REMOVE)	1,713	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0506	7044	BIODEG EROSN CONT LOGS (INSTL) (12")	400	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0506	7046	BIODEG EROSN CONT LOGS (REMOVE)	400	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0506	7001	ROCK FILTER DAMS (INSTL) (TY1)	97	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0506	7011	ROCK FILTER DAMS (REMOVE)	97	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$

Item No.	Description Code	Name of Pay Item with Unit Price in Words	Bid Quantity	Unit	Unit Bid Price	Amount Bid
ADD ALT 1						
		CONSTRUCTION CONTINGENCY	5%	of construction cost		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0100	7001	PREPARING ROW	19.00	STA		
		Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0192	7007	SOIL AMEND	220	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0556	7009	PIPE UNDERDRAINS (TY 9)(6")	1,133	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0194	7011	RDSIDE AMENITY (STONE SLAB)	810	SF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0192	7059	PLANT MATERIAL (MIN 3" CAL)(B&B)	23	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0192	7009	PLANT BED PREP	624	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0192	7016	LANDSCAPE EDGING	169	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0192	7022	LOOSE AGGR GRND COVER	91	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0192	7026	PLANT MATERIAL (4" FLAT)	6,990	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$
0192	7026	PLANT MATERIAL (14/16 BULBS)	9,171	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		_____ Dollars and				
		_____ Cents per unit			\$	\$

Item No.	Description Code	Name of Pay Item with Unit Price in Words	Bid Quantity	Unit	Unit Bid Price	Amount Bid
0192	7026	PLANT MATERIAL (1 GAL)	3,098	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$
0192	7028	PLANT MATERIAL (3 GAL)	24	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$
0192	7002	MULCH	624	SY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$
0192	7003	PLANTING SOIL MIX	412	CY		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$
0170	7001	IRRIGATION SYSTEM	1	LS		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$
0618	7035	CONDT (PVC) (SCH 40) (2 1/2") (BORE)	165	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$
0618	7045	CONDT (PVC) (SCH 40) (6") (BORE)	145	LF		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$

Item No.	Specification Item	Name of Pay Item with Unit Price in Words	Bid Quantity	Unit	Unit Bid Price	Amount Bid
ADD ALT 2						
		CONSTRUCTION CONTINGENCY	5%	of construction cost		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$
0192	7026	PLANT MATERIAL (1 GAL)	-5,056	EA		
		As shown, detailed, and specified, Complete in Place, for the Sum of				
		Dollars and				
		Cents per unit			\$	\$

BID ITEMS:

A. BASE BID
Total of Base Bid Amount \$ _____

B. BID ALTERNATES
Total of ADD ALT 1 Amount \$ _____

C. BID ALTERNATES
Total of ADD ALT 2 Amount \$ _____

PROJECT GRAND TOTAL
\$ _____

Contract Time Estimate (Base Bid + ADD ALT 1 + ADD ALT 2)

Rd: FM 740 Ridge Rd

County: Rockwall

CSJ: 1014-03-063

Project: Median Landscape


Number of Working Days: CSJ: 1014-03-063 = 200 Working Days


Number of Working Days with bad Weather: (Days*1.1) = 220 Weather Days

Number of Barricades in Months (Working Days*1.22/20 Days/Months) = 12.2 Months

CSJ	HIGHWAY	COUNTY	LETTING DATE	MANAGEMENT PLAN IN MONTHS	ESTIMATED TIME BEGIN DATE	WORKING DAYS FROM TDS	CALENDER	CHARGEABLE DAYS	ESTIMATED COMPLETION DATE	BARRICADE MONTHS
1014-03-063	FM 740	ROCKWALL	7/1/2026		10/1/2026	200	Five-day Workweek	244	10/9/2027	12.2

													2
TASK #	Description	Quantity	Unit	Daily Rate	Duration	Pred Task	% Complete	Pred Task	% Complete	Pred Task	% Complete	Start Day	Finish Day
1	MOBILIZATION	1	LS	0.2	5							1	5
2	TRAFFIC CONTROL (INSTL.)	12.2	MO	1.6	8							6	13
3	TEMP SEDMT CONT FENCE (INSTL.)	1,713	LF	3000	1							14	14
5	ROCK FILTER DAMS (INSTL) (TY1)	97	LF	100	1							15	15
4	BIODEG EROSN CONT LOGS (INSTL.) (12")	400	LF	400	1							16	16
6	PREPARING ROW	69.00	STA	3.5	20							17	36
7	PREP ROW (TREE REMOVE) (0"-12" DIA)	138	EA	30	5							37	41
8	PIPE UNDERDRAINS (TY 9) (6")	4,378	LF	300	15							42	56
9	SOIL AMEND	1,419	SY	100	15							57	71
10	RDSIDE AMENITY (BOULDER)	39	EA	8	5							72	76
11	RDSIDE AMENITY (STONE SLAB)	6,351	SF	360	18							77	94
12	LANDSCAPE EDGING	933	LF	1000	1							95	95
13	LOOSE AGGR GRND COVER	1,091	SY	500	3							96	98
14	IRRIGATION SYSTEM	1	LS	0.1	10							99	108
15	PLANTING SOIL MIX	2,001	CY	300	7							109	115
16	PLANT MATERIAL (MIN 3" CAL)	144	EA	15	10							116	125
17	PLANT BED PREP	3,513	SY	320	11							126	136
18	PLANT MATERIAL (4" FLAT)	21,592	EA	2000	11							137	147
19	PLANT MATERIAL (14/16 BULBS)	33,130	EA	2000	17							148	164
20	PLANT MATERIAL (1 GAL)	14,636	EA	1200	13							165	177
21	PLANT MATERIAL (3 GAL)	263	EA	300	1							178	178
22	MULCH	3,513	SY	600	6							179	184
23	TEMP SEDMT CONT FENCE (REMOVE)	1,713	LF	3000	1							185	185
24	BIODEG EROSN CONT LOGS (REMOVE)	400	LF	400	1							186	186
25	ROCK FILTER DAMS (REMOVE)	97	LF	100	1							187	187
26	TRAFFIC CONTROL (REMOVE)	12.2	MO	1.6	8							188	195
27	MOBILIZATION (CLEANUP)	1	LS	0.2	5							196	200

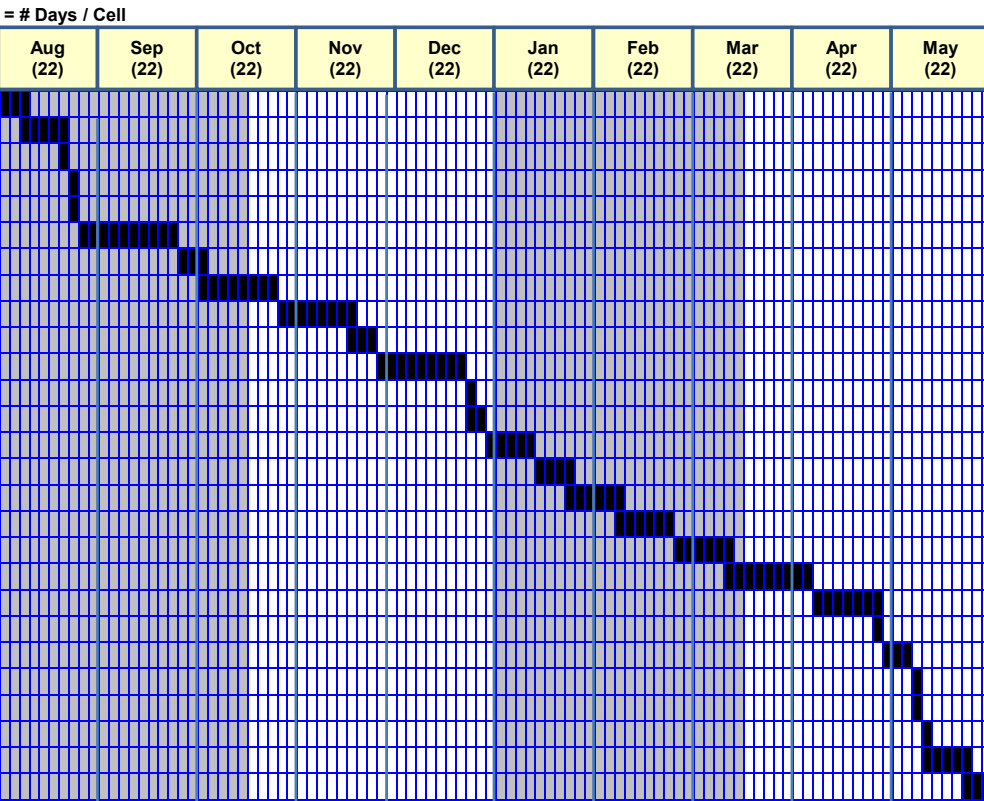



06/12/2026

Item No.	Description Code	Description	Unit	Quantity (Base Bid)	Unit Price	Amount (Base Bid)	Quantity (Add Alt 1)	Amount (Add Alt 1)	Quantity (Add Alt 2)	Amount (Add Alt 2)
		LANDSCAPE								
0100	7001	PREPARING ROW	STA	50.00	\$400.00	\$20,000.00	19.00	\$7,600.00		
0100	7003	PREP ROW (TREE REMOVE) (0"-12" DIA)	EA	138	\$500.00	\$69,000.00	0	\$0.00		
0192	7007	SOIL AMEND	SY	1,199	\$26.70	\$32,024.28	220	\$5,874.00		
0556	7009	PIPE UNDERDRAINS (TY 9) (6")	LF	3,245	\$32.00	\$103,840.00	1,133	\$36,256.00		
0194	7010	RDSIDE AMENITY (BOULDER)	EA	39	\$2,200.00	\$85,800.00	0	\$0.00		
0194	7011	RDSIDE AMENITY (STONE SLAB)	SF	5,541	\$42.00	\$232,710.24	810	\$34,020.00		
0192	7052	PLANT MATERIAL (MIN 3" CAL)	EA	121	\$1,000.00	\$121,000.00	23	\$23,000.00		
0192	7009	PLANT BED PREP	SY	2,889	\$9.50	\$27,444.45	624	\$5,926.94		
0192	7016	LANDSCAPE EDGING	LF	764	\$12.00	\$9,168.00	169	\$2,028.00		
0192	7022	LOOSE AGGR GRND COVER	SY	1000	\$23.00	\$22,997.44	91	\$2,095.56		
0192	7026	PLANT MATERIAL (4" FLAT)	EA	14,602	\$1.80	\$26,283.60	6,990	\$12,582.11		
0192	7026	PLANT MATERIAL (14/16 BULBS)	EA	23,959	\$1.80	\$43,127.03	9,171	\$16,507.01		
0192	7026	PLANT MATERIAL (1 GAL)	EA	16,594	\$10.00	\$165,944.60	3,098	\$30,975.00	-5,056	-\$50,559.60
0192	7028	PLANT MATERIAL (3 GAL)	EA	239	\$30.00	\$7,170.00	24	\$720.00		
0192	7002	MULCH	SY	2,889	\$8.00	\$23,111.12	624	\$4,991.11		
0192	7003	PLANTING SOIL MIX	CY	1,589	\$80.00	\$127,136.65	412	\$32,954.34		
0170	7001	IRRIGATION SYSTEM	LS	1.0	\$160,000.00	\$160,000.00	1.0	\$40,000.00		
0618	7035	CONDT (PVC) (SCH 40) (2 1/2") (BORE)	LF	0	\$52.00	\$0.00	165	\$8,580.00		
0618	7045	CONDT (PVC) (SCH 40) (6") (BORE)	LF	117	\$81.00	\$9,477.00	145	\$11,745.00		
Sub-Total						\$1,286,234		\$275,855		-\$50,560
		TRAFFIC CONTROL		1						
0502	7001	BARRICADES, SIGNS AND TRAFFIC HANDLING	MO	12.2	\$2,000.00	\$24,400.00				
0503	7001	PORTABLE CHANGEABLE MESSAGE SIGN	DAY	375	\$125.00	\$46,875.00				
		EROSION CONTROL								
0506	7039	TEMP SEDMT CONT FENCE (INSTALL)	LF	1,186	\$5.00	\$5,930.00				
0506	7040	TEMP SDMT CONT FENCE (INLET PROTECTION)	LF	527	\$1.50	\$790.50				
0506	7041	TEMP SEDMT CONT FENCE (REMOVE)	LF	1,713	\$1.00	\$1,713.00				
0506	7044	BIODEG EROSN CONT LOGS (INSTL) (12")	LF	400	\$5.00	\$2,000.00				
0506	7046	BIODEG EROSN CONT LOGS (REMOVE)	LF	400	\$1.50	\$600.00				
0506	7001	ROCK FILTER DAMS (INSTL) (TY1)	LF	97	\$40.00	\$3,880.00				
0506	7011	ROCK FILTER DAMS (REMOVE)	LF	97	\$15.00	\$1,455.00				
0500	7001	MOBILIZATION	LS	1	\$100,000.00	\$100,000.00				
		CONSTRUCTION CONTINGENCY	of construction cost	5%	\$64,311.72	\$64,311.72		\$13,792.75		-\$2,527.98
Sub-Total						\$251,955.22		\$13,792.75		-\$2,527.98
TOTAL:						\$1,538,190		\$289,648		-\$53,088
GRAND TOTAL (BASE BID + ADD ALTS)										\$1,774,750

	Date	Description
1	07/28/2026	IFB Addendum #2



06/12/2026

Signature of Registrant & Date
THE STANDARD SHEETS SPECIFICALLY IDENTIFIED ABOVE
HAVE BEEN SELECTED BY ME OR UNDER MY RESPONSIBLE
SUPERVISION AS BEING APPLICABLE TO THIS PROJECT.


ROCKWALL FM 740
STREETSCAPE IMPROVEMENTS



City of Rockwall
The New Horizon

MESA

2001 North Lamar St,
Suite 100
Dallas, Texas 75202
214.871.0568 tel
214.871.1507 fax
mesadesigngroup.com



Texas Department of Transportation

© 2025

ESTIMATE AND QUANTITY
SHEETS

DESIGN	FED.RD. DIV.NO.	FEDERAL AID PROJECT.		HIGHWAY NO.
GRAPHICS	6	(SEE TITLE SHEET)		FM 740
	STATE	DISTRICT	COUNTY	SHEET NO.
CHECK	TEXAS	DALLAS	ROCKWALL	6
CHECK	CONTROL	SECTION	JOB	
	1014	03	063	

CSJ: 1014-03-063: FM 740 RIDGE ROAD MEDIAN LANDSCAPE IMPROVEMENT COST ESTIMATE

Item No.	Description Code	Description	Unit	Quantity (Base Bid)	Quantity (Add Alt 1)	Quantity (Add Alt 2)
		LANDSCAPE				
0100	7001	PREPARING ROW	STA	50.00	19.00	
0100	7003	PREP ROW (TREE REMOVE) (0"-12" DIA)	EA	138	0	
0192	7007	SOIL AMEND	SY	1,199	220	
0556	7009	PIPE UNDERDRAINS (TY 9) (6")	LF	3,245	1,133	
0194	7010	RDSIDE AMENITY (BOULDER)	EA	39	0	
0194	7011	RDSIDE AMENITY (STONE SLAB)	SF	5,541	810	
0192	7052	PLANT MATERIAL (MIN 3" CAL)	EA	121	23	
0192	7009	PLANT BED PREP	SY	2,889	624	
0192	7016	LANDSCAPE EDGING	LF	764	169	
0192	7022	LOOSE AGGR GRND COVER	SY	1000	91	
0192	7026	PLANT MATERIAL (4" FLAT)	EA	14,602	6,990	
0192	7026	PLANT MATERIAL (14/16 BULBS)	EA	23,959	9,171	
0192	7026	PLANT MATERIAL (1 GAL)	EA	16,594	3,098	-5,056
0192	7028	PLANT MATERIAL (3 GAL)	EA	239	24	
0192	7002	MULCH	SY	2,889	624	
0192	7003	PLANTING SOIL MIX	CY	1,589	412	
0170	7001	IRRIGATION SYSTEM	LS	1.0	1.0	
0618	7035	CONDT (PVC) (SCH 40) (2 1/2") (BORE)	LF	0	165	
0618	7045	CONDT (PVC) (SCH 40) (6") (BORE)	LF	117	145	
		TRAFFIC CONTROL		1		
0502	7001	BARRICADES, SIGNS AND TRAFFIC HANDLING	MO	12.2		
0503	7001	PORTABLE CHANGEABLE MESSAGE SIGN	DAY	375		
		EROSION CONTROL				
0506	7039	TEMP SEDMT CONT FENCE (INSTALL)	LF	1,186		
0506	7040	TEMP SDMT CONT FENCE (INLET PROTECTION)	LF	527		
0506	7041	TEMP SEDMT CONT FENCE (REMOVE)	LF	1,713		
0506	7044	BIODEG EROSN CONT LOGS (INSTL) (12")	LF	400		
0506	7046	BIODEG EROSN CONT LOGS (REMOVE)	LF	400		
0506	7001	ROCK FILTER DAMS (INSTL) (TY1)	LF	97		
0506	7011	ROCK FILTER DAMS (REMOVE)	LF	97		
0500	7001	MOBILIZATION	LS	1		
		CONSTRUCTION CONTINGENCY	of construction cost	5%		

	Date	Description
1	07/28/2026	IFB Addendum #2



Signature of Registrant & Date

THE STANDARD SHEETS SPECIFICALLY IDENTIFIED ABOVE HAVE BEEN SELECTED BY ME OR UNDER MY RESPONSIBLE SUPERVISION AS BEING APPLICABLE TO THIS PROJECT.


ROCKWALL FM 740
STREETSCAPE IMPROVEMENTS



City of Rockwall
The New Horizon

MESA

2001 North Lamar St,
Suite 100
Dallas, Texas 75202
214.871.0568 tel
214.871.1507 fax
mesadesigngroup.com



Texas Department of Transportation
© 2025

QUANTITY SUMMARY SHEETS

DESIGN	FED.RD. DIV.NO.	FEDERAL AID PROJECT.		HIGHWAY NO.
GRAPHICS	6	(SEE TITLE SHEET)		FM 740
	STATE	DISTRICT	COUNTY	SHEET NO.
CHECK	TEXAS	DALLAS	ROCKWALL	7
CHECK	CONTROL	SECTION	JOB	
	1014	03	063	
